
CAMBRIAN / SOLANA DATA / 01

Solana: time to revisit the priority.

Our dev team already owns Solana.
We kept it at lower priority for six months.

Three paths to reliable customer data

Cambrian · 12 October 2026

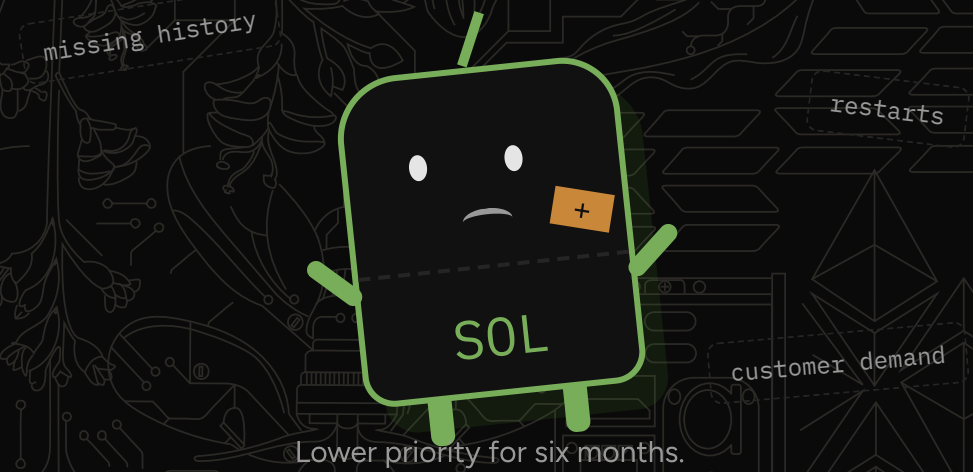

Lower priority for six months.

Customer demand now calls for a priority decision and dedicated dev-team capacity.

Basis: team facts + Lhava repo + live ClickHouse metadata.

Customer demand brings Solana back into focus.

01

Positions

What did I own?
When did it change?

→

02

Fees

What did I earn?
Can I reconcile it?

→

03

History

2024 required
2023 is a later option.

> Lhava needs the actions inside each transaction, including nested LP strategy calls.

Reliable delivery matters more to this customer than being first at chainhead.

[R1] Requirements • [R2] Meteora sample validation.

CAMBRIAN / SOLANA DATA / 03

Lower priority left these issues for the next investment.

01 · Old hardware

Restarts → repeated work

02 · Missing instructions

Incomplete history → investigation



03 · Storage limits

Expiry rules → lost history

04 · Export friction

Moving data → vendor dependency

The existing dev team needs allocated time to address these reliability and history gaps.

[U] Team-provided facts; current invoice and incident logs were not audited.

We made room by letting history disappear.

15.36 TB shared disk, measured



WITHIN SOLANA

2.53 TB

Tables that expire rows after one month.

WITHIN SOLANA

1.32 TB

Raw token balances with short retention.

WITHIN SOLANA

0.134 TB

Retained Meteora DLMM data.

Free space today is not a capacity plan for keeping several years.

[Q1–Q5] Read-only ClickHouse system metadata, 12 Oct 2026.

Give it the right-sized room.

CUSTOMER DATASET · MODELED

0.56 TB

Meteora positions + fees since 2024.
0.87 TB after another year.

RAW BALANCES · SCENARIO

~40 TB

Every balance change since 2024.
~55 TB if we add 2023.

2023	2024 → today	Next 12 months
Optional; Meteora size unmeasured	Customer's required history	Keep collecting, keep retaining

Different datasets, different fidelity. Raw balances assume a constant recent daily rate. Full raw blocks remain unsized.

Start with selected customer datasets; price full raw history separately.

[R3] Lhava storage model, 6 Oct • [M1] Reproducible arithmetic.

Three paths for the next investment.

PATH 1

Repair

Stay with Pinax

Improve servers. Rebuild from 2023.

Vendor dependency continues.

PATH 2 · PREFERRED IF VALIDATED

Bridge

Recover, then own

Backfill 2024. Export. Move future collection.

More work; better control.

PATH 3

Start

Own from now

Build on onstream immediately.

2024 coverage remains unresolved.

All three require data unification and customer-level validation.

[U] Paths from the brief; OVH serving placement is a proposed implementation.

Path 1 · Improve the current setup.



What improves

Replace unreliable hardware; agree storage expansion, source quality and export rights.

What stays

Pinax operates the source and hardware. We maintain decoders, history and deduplication.

What blocks it

More hardware cannot restore instructions already missing from the archive.


Rebuild beside the current data; replace only the windows that pass checks.

[U] Team facts • [E1] Planning estimate: ~20 engineer-days, range 15–27.5.

Path 2 · Recover its past. Own its future.

RECOVER THE PAST

PROTECT THE FUTURE

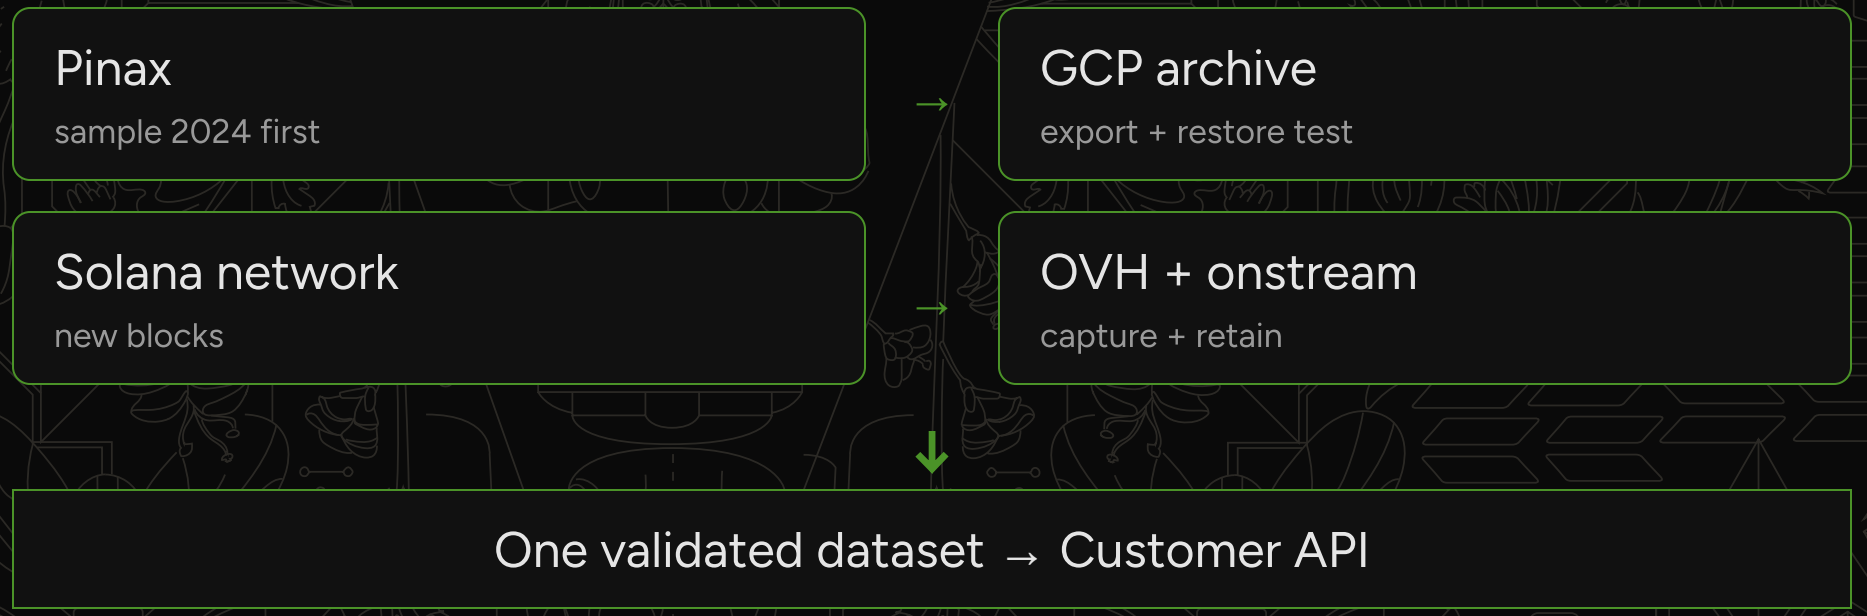

Proposed serving: ClickHouse + API on OVH

Exit only after quality, restore, live stability and Base continuity pass.

Preferred path if Pinax's historical sample meets the customer's needs.

[U] Existing onstream prototype • [E2] ~30.5 engineer-days, range 20–42.5.

Path 3 · Build live capture. History still waits.

2024 → now

Historical gap remains.

Preserve useful existing data.

? ? ? ? ?

START HERE

Now → future

Our collection. Our retention.

Our maintenance responsibility.


● — ● — ● — ●

> Onstream can replay available history. It cannot recreate instructions a source discarded.

Choose this if history cannot be recovered and the customer accepts a narrower scope.

[U] Archive access is difficult • [E3] ~25 engineer-days, range 17.5–35.

Every path needs data unification.



Repair known gaps

Add v2 and rebalance decoding; repair affected months; model open/close events.

Make retries safe

Use stable event IDs and checkpoints. Verify amounts, instruction paths and finalized blocks.

Expose quality

Label verified, reconstructed and unavailable fields. Publish coverage by date and endpoint.

Better servers reduce failures; they do not remove the need for safe replay.

[R2, R4] Known gaps + effort model • [C1–C4] ClickHouse rules.

A real operating budget for a real product.

PATH 1 · CURRENT BILL

$2,000

Per month for the Pinax bundle.
+ server/storage upgrade quote

PATHS 2 / 3 · PLANNING ALLOWANCE

$2,700–5,500

Per month for our Solana platform.
+ Base replacement + archive + transfer

Node
$1.5–3k

Database + API
$1–2k

Monitoring + backup
$0.2–0.5k

Selected 0.56 TB GCP archive ≈ $10/month. Pinax overlap adds $2k/month until exit.
Allowances exclude labor, extra HA replicas, raw-block archive, source fees, setup and tax adjustments.

Archive storage is cheap relative to running reliable collection and APIs.

[P1] GCS published rate • [P2] OVH price reference • [M1] Budget assumptions.

Allocate dev-team time to the chosen path.



PLANNING RANGES

15–27.5 / 20–42.5 / 17.5–35

Engineer-days, paths 1 / 2 / 3.

ADD POOL STATE + FEES

+14 days

Adjusted estimate; range 8.5–19.

ONGOING ONSTREAM CARE

1–2.5 days/mo

Assumed maintenance reserve.

One engineer-day means one person working one day; it is not a calendar deadline.

[R4] H1/H2 effort baseline • [E1–E3] Assumed platform work and ranges.

About 32 days to recover the 2024 backlog.

~32 historical days per day
user-reported replay rate

2024 → 11 OCT 2026

~31.7 days

1,015 historical days ÷ 32.
About 32 days of continuous replay.

INCLUDING 2023

~43.1 days

Another 365 historical days adds ~11.4 days.
1,380 historical days ÷ 32.

Replay only: assumes the reported rate is sustained and history is available.
If 32× also includes live ingestion, catching up the 2024 backlog takes ~32.7 days.
Engineering, transfer, validation and interruptions require separate allowances.

Allow about 32 days of continuous replay, plus transfer, validation and interruptions.

[U] User-reported ~32 historical days/day • [M1] Replay arithmetic.

Three gates before we leave Pinax.

01

History

2024 source passes.
Missing fields are explicit.

→

02

Portability

Export agreed.
Restore works. Base has a plan.

→

03

Readiness

Restarts and upgrades tested.
Customer accepts output.

> If history fails, Path 3 needs customer acceptance of a shorter history.


Discussion: is 2024 completeness essential, and what gaps will Lhava accept?

[R1–R2] Customer evidence • Proposed acceptance gates, not existing guarantees.

Agree the priority. Allocate team capacity.

Data	Prove the 2024 history.
Platform	Validate onstream; reserve maintenance time.
Operations	Secure export terms + Base continuity.
Product	Agree the output with Lhava.

First checkpoint: 5 working days / 2.5–4 engineer-days



Ready for the next priority.

Give the existing dev team time and budget for the pilot. Then choose with evidence.

Notes: press N • Sources and calculations included with this deck.
